ARVIN-EDISON WATER STORAGE DISTRICT

REPORT OF DISTRICT OPERATIONS

June 2026

Sycamore Channel Dirt Work

20401 East Bear Mountain Blvd.
Mailing: P.O. Box 175
Arvin, CA 93203-0175

Phone: 661-854-5573
Fax: 661-854-5213
E-mail: arvined@aewsd.org
Website: aewsd.org

WATER SUPPLY

Friant Division Central Valley Project (CVP)

- The initial 2026 Water Year allocation was announced on February 26, 2026, at 100% Class 1, which amounts to 40,000 AF, and 0% Class 2. To date, the initial allocation has remained unchanged
- Exhibit "A" provides additional supply information for 2026 Water Year supplies.

San Joaquin River (SJR) Restoration Program (SJRRP)

- On May 15, 2026, the SJRRP transmitted to the Restoration Administrator (RA) the final Restoration Allocation for the 2026 Water Year. The allocation is based on a 50% Exceedance forecast of 1,438,000 AF of natural river runoff, which is a Normal-Dry water year type and results in a restoration flow allocation of 281,739 AF.
- The RA submitted the final schedule on June 1, 2026, which recommends the release of 205,755 AF of Restoration Flows to the river, which is less than the restoration allocation due to downstream capacity limitations, leaving approximately 80,000 AF of potential Unreleased Restoration Flows (URF).
- On March 19, 2026, 10,479 AF (net) of URFs were made available to Friant Class 1 contractors, of which the District's portion is 530 AF. This quantity must be used by April 15, 2026.
- On May 5, 2026, 10,002 AF (net) of URFs were made available to Friant Class 2 contractors, of which the District's portion is 2,224 AF. This quantity must be used by May 24, 2026.
- On June 9, 2026, 51,299 AF (net) of URFS were made available to Friant Class 2 contractors, of which the District's portion is 11,409 AF. This quantity is schedulable and must be used by February 28, 2026.
- To date, the District has received approximately 7,300 AF of Recapture supplies.
- District's Recovered Water Account (RWA) balance is approximately 68,000 AF. RWA credits allow the District to purchase water for $10/AF during wet periods (uncontrolled season but subject to canal prorate) when RWA water is declared.

Other CVP Contractors

- The current North-of-Delta 2026 allocation is 100% for Agricultural Service Contractors.
- The current South-of-Delta 2025 allocation is 25% for Agricultural Service Contractors, this includes the District's Fresno County supply which amounts to 750 AF. However, due to Delta water quality concerns and pumping limitations, it's possible that not all the 750 AF will be made available to the District.

State Water Project (SWP)

- The current California Department of Water Resources 2026 State Water Project allocation is 45%.

Kern River

- The Kern River 2025 April through July runoff is 66% of average.

Water Bank Facilities

- The District is expected to recover approximately 54,000 AF of previously banked supplies in Water Year 2026.

Metropolitan Water District (MWD) Program

- MWD account balance remains at 100,201 AF.
- The District has approval from the State Water Resources Control Board regarding a Petition for a Consolidated Place-of-Use (CPOU), which now expires on July 22, 2026, to deliver CVP water to MWD.
- The CPOU petition includes the ability to exchange all types of Arvin-Edison supplies with MWD including unbalanced exchanges.
- The District's 10-year NEPA documentation is complete and approved until March 2034.

Rosedale-Rio Bravo Water Storage District (RRBWSD) Program

- The District's account balance in RRBWSD on March 2026 was approximately 35,000 AF. District anticipates to receive 5,000 AF of returned bank supplies from RRBWSD in during Water Year 2026, leaving approximately 30,000 AF in the account balance.

District Partnerships

- The District received a ten-year approval (through Water Year 2035) from USBR to transfer and exchange Friant Division CVP water to Kings River Area Agencies and Kern County Districts.
- The District has participated in water management programs with the following districts/agencies in Water Year 2025 to date:

Fresno County	Rosedale Rio Bravo WSD
Madera Irrigation District	SJRRP Recapture/Recirculation
Del Puerto Water District	Chowchilla Water District
City of Bakersfield	Kern-Tulare Water District
Delano-Earlimart Irrigation District	Kaweah Delta Conservation District

WATER DEMAND

District turnout deliveries (not including on-farm recharge) for the month were 19,894 AF.

- The following is a summary of surface water deliveries for June 2026.

Water Type	Month of June		Water Year to Date	
	10 Yr. Avg.	2026	10 Yr. Avg.	2026
SWSA	18,108	19,811	49,790	60,240
In-Lieu		0		0
Temporary		0		0
Spreading*	n/a	83	n/a	2,883
	Total	19,894	Total	63,123

*Direct spreading, including Landowner (on-farm) Recharge

- Exhibits "B-1", "B-2", and "B-3" illustrate the delivery data.
- The month's peak daily in-District demand was 509 cfs, which occurred on the 16th.
- Exhibit "C-1" details Canal Water Quality information.
- Exhibit "C-2" presents the Aquatic Pest Control Treatments ($56,151 for Calendar Year 2026).

GENERAL

- District vehicles consumed an estimated 4,232 gallons of fuel during the month (average fuel efficiency of 13.32 mpg).
- There were 521 hours lost due to illness and 160 hours lost due to on-the-job injuries.
- Exhibit "D" highlights precipitation, temperature, and wind speed.
- Exhibit "E" summarizes energy consumption and power demand.

ENGINEERING DEPARTMENT ACTIVITIES

Routine Activities

- Review and accounting of District's water supply and related contracts.
- Administration or proposals of water management and wheeling agreements.
- Groundwater level surveys and associated exhibits.
- Water quality testing.
- ArcGIS database updates/maintenance (facilities, water service areas, boundaries, etc.).
- CIMIS station management (https://cimis.water.ca.gov/Stations.aspx).
- Land use/crop surveys with data entry.
- Monthly/annual reports regarding water deliveries, water use, and energy use.

Grants & Funding Opportunity Updates

Project Name	Drought Recovery Wells and Conjunctive Use Modeling Tool	Forrest Frick Unit Project		White Wolf Groundwater Sustainability Agency	Groundwater Flow Model and Decision Support Tool	North Canal Spreading Works Expansion Project		DiGiorgio Unit Phase 2b-5 Project		Tejon Spreading Works Project
Grant Name	USBR 2023 WaterSMART Drought Recovery Program Grant	DWR Round 2 Integrated regional Water Management Grant	Community Project Funding Grant	DWR – SGM Round 2 Grant	USBR 2023 Water SMART Applied Science Grant	DWR – Flood Diversion Recharge Enhancement (FDRE) Grant	FY2026 Community Project Funding Grant	USBR 2024 Planning and Project Design Grant	FY 2027 Community Project Funding Grant	USBR 2026 Water SMART Drought Response Program
Grant Type	Federal	State	Federal	State	Federal	State	Federal	Federal	Federal	Federal
Grant Status	Awarded	Awarded	Awarded	Awarded	Awarded	Awarded	Secured	Awarded	Funding Request Submitted	Preparing Application
Grant Amount	$2 Million	$2 Million	$3.25 Million	$4.8 Million	$95,000	$999,500	$2 Million	$308,170	$5 Million	$1,500,000
Notes	*Final Grant Report Due 7/29/26*		*Grant Agreement Received 4/3/26*	*Final Grant Report Due 8/31/26*	*Grant is complete*	Grant is complete	*1/8/26 - Valadao press release issued for funding recipients* *2/4/26 – Received official notification from EPA*		*6/17 – Project was selected and approved by the Appropriations Committee. Pending Appropriations Bill Approval.*	*Grant Application due 7/28/26*

- NRCS landowner incentive programs assist with implementing various conservation activities, including but not limited to, irrigation system improvements, filtration needs, water/nutrient/pest management, and engine replacement:
  - Phone (661) 336-0967
  - Website (www.ca.nrcs.usda.gov)
- North West Kern Resource Conservation District provides discounted on-farm irrigation distribution uniformity and efficiency testing
  - Phone (661) 281-2746
  - Website (http://northwestkernrcd.org)

AEWSD Current Construction Projects

	N24 & N26 Recovery Wells – Drilling & Equipping	N24 & N26 Recovery Wells – Electrical	S39 & T102 Wells - Drilling & Equipping	S39 & T102 Wells – Electrical
	Bakersfield Well & Pump	A-C Electric	Bakersfield Well & Pump	Bakersfield Well & pump – Twin Electric as sub-contractor
Construction Start Date	March 2025	March 2025	November 2025	June 2026
Punch List	March 2026	March 2026	November 2026	November 2026
Final Project Close-Out	March 2026 – SUBSTANTIAL COMPLETION ISSUED	March 2026 – SUBSTANTIAL COMPLETION ISSUED	December 2026	December 2026
Current Construction Contract Costs	$2,144,560 (Change Order #1-6 for revised quantities and additional days due to material delays)	$557,706.37 (Change Order #1-4 for fencing, external display for soft starts and additional days due to material delays)	$2,229,092	$593,681
Total Grant Funding	$2,000,000 (Federal Share) $2,160,421 (Recipient Share)		N/A	N/A
Notes	**Time Extension approved. Grant Funding needs to be spent by March 31, 2026. Final grant report due July 29, 2026.*			

	NCSW Expansion – FDRE – 1st Contract	NCSW Expansion – FDRE - 2nd Contract	White Wolf Subbasin 850 Canal Intertie	White Wolf Temp Water Program	Frick Unit Phase 2 – Main Line
	Pay Dirt Construction	Super Ag Construction	Laurel Ag & Water	Superior Ag Construction	Superior Ag Construction
Construction Start Date	July 2025	December 2025	July 2025	October 2025	February 2026
Punch List	November 2025	May 2026	March 2026	March 2026	October 2026
Final Project Close-Out	January 2026 - COMPLETE	June 2026 - SUBSTANTIAL COMPLETION ISSUED	April 2026 – NOTICE OF COMPLETION ISSUED	April 2026 – NOTICE OF COMPLETION ISSUED	October 2026
Current Construction Contract Costs	$1,048,815.25 (Change Order #1-5 approved to add raising of exterior levees work, no cost time extension and rip rap)	$763,699.83 (Change Order #1 approved 12/3/25 to extend completion date due to raising of exterior levees work. Change Order #2 approved for IBS boxes and time extension for material delay)	$649,563.47 (Change Order #1-5 approved for extra work, weather delays and no cost time extension)	$785,012.69 (Change Order #1-3 approved for extra work, weather delays and no cost time extension)	$4,380,570.93 (Change Order #1-3 approved for weather delays, revisions to the mainline & Lateral N0-A, and unknown utility line conflicts)
Total Grant Funding	$999,500		$925,000	$1,345,000 ($212,000 is allocated to WRMWSD)	$1,000,000 (DWR Estimated Remaining Funds after Phase 1)
Notes	**FDRE Grant Funding needs to be spent by March 31, 2026. Final reimbursement deadline is May 1, 2026*		**Grant Amendment Approved to extend out to 6/30/2026*	**Grant Amendment Approved to extend out to 6/30/2026*	EPA Funding will be used for Phase 3 – Laterals *DWR Funding to be spent by March 2027.*

AEWSD Upcoming Construction Projects

	Frick Unit Phase 3 - Laterals	North Canal Spreading Works Expansion
Bid Advertisement	July 7 – July 28, 2026	TBD
Board Approval	September 8, 2026	TBD
Anticipated Notice to Proceed	September 21, 2026	TBD
Mobilization Start	October 2026	TBD
Projected Completion Date	July 2027	TBD
Current Estimated Costs	$4,195,000	$3,151,000
Total Grant Funding	$3,250,000 (EPA Grant Funding will be allocated to Phase 3 of the Frick Unit Project)	$2,000,000 (EPA Grant Funding)
Notes	**DWR Grant Funds must be spent by March 31, 2027* **SPA Grant Funds must be spent by June 30, 2028*	**** Bidding and Construction start are dependent on EPA grant agreement.***

Other Activities

- Administration and accounting of on-going water management programs.
- Technical support and review of ongoing projects/studies such as:
  - Potential Interconnections with other Districts.
  - Pump Replacement Program.
  - Turnout Modification Requests.
  - Temporary and/or In-Lieu Water Service Contract Requests.
  - Pump Efficiency Testing.
  - Real Time Water Quality Monitoring.
  - Stand tank Painting Project.
  - Stand tank and pressure vessel inspections.

SGMA Activities

- The Kern Subbasin continuation hearing was held September 17, 2025. The State Water Resources Control (SWRCB) board was satisfied with the 2025 GSP and decided to send the Subbasin back to the California Department of Water Resources. The official letter from the SWRCB sending the Subbasin back to the DWR was issued December 8, 2025. DWR has up to two years to review the plan.
- The Kern Subbasin 2025 GSP is now being implemented.
- Continued coordination meetings and outreach activities.
- Attended various GSA meetings.
- Collected groundwater levels and water quality data.

- Continued coordination efforts with South of Kern River GSAs (posted on website www.sokrgsp.com).
- Continued implementation and coordination efforts with White Wolf Subbasin GSA and GSP (posted on website www.whitewolfgsa.org).

Requests for Information/Easements/Planning Notices

- Water supply
- Water costs
- Historical groundwater levels
- Monitoring well conversions
- Water quality
- Land use data
- Easements and/or right-of-way encroachments
- Reviewed/responded to multiple planning notices
- Reviewed/responded to environmental documents as necessary
- Responded to As Built Requests

Power Related Activities

- Revised power purchase agreements with White Pine Renewables for a total of 10 MW solar production.
- Managed Electrical Distribution Expansion Study process.
- Reviewed Renewable Portfolio Standards balances.
- Coordinated planned PG&E outages, meter repairs and reviewed Trimark and RBI invoices.
- Performed weekly load forecast reviews.
- Reported on PWRPA power accounting.
- Reviewed PWRPA monthly invoices for billing anomalies/meter reconciliations.
- Reviewed power reconciliation reporting tool.
- Worked on On-Farm Solar RECS agreements and reporting.
- Maintained Wells First Off List (efficiency rating).
- Performed Load forecast updates and rate analysis.
- Coordinated with PG&E on meter inventory information.
- Coordinated new power service design and construction projects.
- Coordinated monthly landowner Groundwater meter reads, repairs and prepared reports.

SPREADING WORKS OPERATIONS (WELLFIELDS AND BASINS)

- Exhibit "F" summarizes wellfield production to date.
- Exhibit "G-1" summarizes gross direct spreading to date.
- Exhibits "H-1" and "H-2" summarize current static and/or pumping water in table and graphic forms.

Installed New Signage for the Bakersfield Office

Continued to Update Signage Throughout the District

Arvin-Edision Water Storage District

123526001-WELL

Well Field Management

Well Repair Status Report

July 06, 2026

Well Number	Year Built	Age (Years)	Cased Depth (ft)	Previous Well Condition Rating	Current Status	Problem	Notes/Discussion
Sycamore 13	1967	59	840	Acceptable	Permanently Out of Service	Apparent Pump Failure	o Well needs to be abandoned in some manner after pump was not able to pulled from well. o The pump would not come free and the column/tube/shaft ultimatedly separated 220' down. o I recommend we install a locking cap on the well head and leave it as is.

OPERATIONS DEPARTMENT ACTIVITES

Routine Activities

- Operated District's water distribution and delivery systems (canal, reservoirs and wells).
- Conducted monthly safety meetings.
- Performed monthly meter reads at Turnouts and Pump Plants (water and power).
- Maintained weed control at Pump Plants, Turnouts, Air-Vents, and Isolation Valves.
- Monitored Forrest Frick Pumping Plant operations and Intake Canal water levels.
- Inspected control systems at Pump Plants (Transducers, Cla-valves, etc.).
- Replaced burned out Pump Plant lights and panel bulbs.
- Monitored flows and levels at the Intake, North and South Canal.
- Applied warning labels on Turnouts.
- Daily wellfield readings.
- SGMA monthly well readings.
- Monthly safety meeting.

Isolated and Repaired Turnout M-22

Installed Meter Integrity Modules on Turnouts T-67, W-17 & W-37

Additional Activities

- Replaced locks and chains on various Intake gates.
- Rebuilt various leaking mainline air vents.
- Charged WildEye external batteries Districtwide.
- Re-configured 36 Turnout's WildEye devices Districtwide.
- Re-calibrated WildEye device on Sycamore Well #1.
- Re-programed Turnout W-19 meter.
- Replaced Turnout A-62, C-21, C-44, E-91, A-52, T-30, T-6, W-37, W-55, and W-62 WildEye device for warranty.
- Replaced Turnouts M-17, W-20 and W-68 meters.
- Installed directional antenna on Turnout T-30 for WildEye device.
- Installed Heli-Coil on Turnout M-17 flange.
- Installed Meter Integrity Module (MIMS) on Turnouts T-67, W-17 and W-37.

Underground Service Alert (USA) Report

- District initiated 2.
- Responded to 189 USA notices to locate District underground facilities.
  - 5 required markings of District facilities.
  - 105 were renewals.
  - 75 with no conflicts.

Power Outages and/or Interruptions Involving the Following Systems

Power Interruptions													
FFPP		BR		S32	1	S68	1	S88	1	OFFICE		SYC	1
N1		N41	1	S38	3	S73	1	S93	1	INTERTIE		TEJON	1
N8	1	N55	1	S64	1	S78		EOC		NC		CVC	

Lateral Prorates

Prorated Laterals (days)											
N1	0	N8	1	N24	0	N41	0	N55			28
S32	0	S38	25	S64	1	S73	20	S88	0	S93	18

Facility Improvements (Repairs-R or New-N)

Meters-N		Valves-N	
W-20	W-68		
M-17			

MAINTENANCE DEPARTMENT ACTIVITIES

Routine Activities

- Performed weekly yard duties at Headquarters.
- Cleared-out forebays at North and South Canal.
- Organized Maintenance Warehouse.
- Maintenance of the CIMIS Station.

Additional Activities

- Serviced CAT 430 Backhoe.
- Installed a new clutch on the CIMIS Diamondback Mower.
- Performed a disk repair by reinforcing the frame.
- Cleaned out the Mountain Stretch Siphons.
- Installed a bypass at Pump Plant N55-P10.
- Constructed canal weir structures at Sycamore Spreading Works.
- Installed two Victaulic couplers at Tejon Spreading Works Unit #1.
- Cleaned out the Tejon Spreading Works Channel.
- Repaired pinhole leaks on Turnouts T-29 and T-47.
- Repaired the S93-A lateral Air Release Valve (ARV).
- Installed additional lights to the Howard Frick Pumping Plant sign.

Continued Construction of Canal Weir Structures at Sycamore Spreading Works

Rewelded Equipment Frame for a Disc Repair

Cleaned Out Siphons Along the Mountain Stretch

Mechanic's Shop Repair Activities

- Weekly inspection on gas tank and pump.
- Fixed Tire on John Deer backhoe.
- Fixed pony motor on water truck.
- Fixed door on Challenger tractor.
- Fixed all gangs on Krause disc.

Part	Repair/Replaced	Part	Repair/Replaced
Routine Service	12	A/C Service/Heater	4
Brakes	4	Belts	0
Tires	10	Headlights/Taillights	0/2
Tire Repairs	5	Shocks	0
Rotors/Drums /Wheel Bearings	1/1	Wiper Blades/Engine Washes	6/3
Batteries	1	Cabin Filter	6
Fuel Filters	3	Trailer Lights/Spotlights	0/1
Tune-ups	1	Cleaned Throttle Body	3
Clean TPS Sensor	3	Misc.	5

PUMP DEPARTMENT ACTIVITIES

Routine Pump Maintenance Activities

- Replaced various pump packings.
- Lubricated pump bearings at various Pumping Plants.
- Maintained drip oil on District Wells.
- Inspected and maintained Air Compressors.
- Inspected and/or adjusted Traveling Water Screens/Moss Screens.
- Cleaned out or replaced Yardney filter for the Moss Screens sprayer pumps.

Replaced Valves at Forrest Frick Pumping Plant

Additional Activities

- Serviced the Compressors on the North side of the District.
- Performed annual oil changes at Forrest Frick Pumping Plant units #1-8.
- Repaired the stuffing box on a vertical pump at the Balancing Reservoir unit #2.
- Replaced the bad flight guides for the Moss Screens at Pumping Plants N1-P1 and N41-P1.
- Replaced a 300 HP Vertical Motor at Sycamore Well #20.
- Replaced a 100 HP motor at Pump Plant N1-P5 unit #2.
- Replaced a bad 50 HP horizontal motor and a rotating element at Pump Plant N55-P8 unit #1.

Performed Repairs on Multiple Twin Moss Screens

- Replaced a vertical 10 CFS pump at Pump Plant S38-P1 unit #2.
- Replaced a bad 200 HP horizontal motor at Pump Plant S73-P2 unit #2.
- Replaced a 200 HP Horizontal Motor at Pump Plant S93-P3 unit #2.
- Replaced a sump pump at Pump Plant S93-P2.

- Removed all the old rotating elements from the old pumps at Headquarters to be repaired for inventory.
- Replaced a 10 CFS rotating element at Pump Plant N1-P2 unit #2.
- Replaced a 5 CFS rotating element at Pump Plant N1-P8 unit #1.
- Replaced a 2.5 CFS rotating element at Pump Plant N55-P15 unit #2.
- Removed and repaired the Moss screen at Pump Plant N55-P1 (North Screen) due to a broken shaft.
- Replaced a broken chain, moss screen and motor at Pump Plant S64-P1.
- Repaired a 2" PVC pipe off the manifold for the sprayers bypass at Pump Plant S64-P1 unit #5.
- Replaced a broken spring on a 16" check valve at Pump Plant S64-P2 unit #2.
- Repaired a coupler insert at Pump Plant S73-P2 unit #5.

PUMP & MOTOR REPAIR SUMMARY

	Pumping Plant/Wells	Unit	Size	Time/Hours	Reason
Vertical Pumps	S38-P1	2	10 CFS	04864.5	Plastic material stuck in the impellers
	S38-P1	4	5 CFS	46792.5	Bad Bushings
	S64-P1	3	10 CFS	06307.9	Bad Bushings Excessive vibration
Vertical Motors	Sycamore	20	300 HP	N/A	Bad Leads
Horizontal Pumps	N55-P8	1	2.5 CFS	0259.1	Bad Ware Rings
	N1-P2	1	10 CFS	06077.6	Bad Bearings
	N55-P15	2	2.5 CFS	24799.7	Bad Bearings
	N1-P8	1	5 CFS	37820.2	Bad Bearings
Horizontal Motors	S93-P3	2	200 HP	22260.9	Bad Windings
	S73-P2	4	200 HP	02179.1	Bad Windings
	N55-P8	1	50 HP	401593	Bad Stator
	N1-P5	2	100 HP	07102	Bad Bearing
	N55-P15	2	50 HP	24801.4	Smelled Burnt

CONTROLS DEPARTMENT ACTIVITIES

Routine Activities

- Processed monthly purchase orders.
- Performed electrical maintenance and repairs.
- Monthly inventory.

Distribution System Improvements (Repairs-R or New-N)							
Starter Controls	**Contactors / Soft Start**	**Aux. Contact Block**	**Motor Control Panels**	**Battery Back-up Units**	**Circuit Breakers**	**Hour meters**	**Trip Units**
	N – S64-P1 unit #3 – replaced softstart power pole					N – N55-P8 unit #1 – replaced hour meter	
	N – N1-P1 unit #1 – replaced softstart power pole						

Distribution System Improvements (Repairs-R or New-N)							
Radios	**PLC's or Control Mods.**	**Photocell / Lights**	**Wiring**	**Valve Controllers or Limitorque**	**Coils**	**Relays / Thermal O/L**	**Fuses / Transducers**
N -- Soth H Checkgate – replaced new cell comm module for data communication			N – N55-P4 unit #2 – replaced underground motor cable, shunt straps, contact insulators & motor starter contactors	N – N1-P1 unit #1 – replaced limitorque forward-reverse motor contactor		N – N55-P15 unit #2 – replaced machine tool relay.	N – S73-P4 – replaced pressure transducer & 24VDC power supply
			N – Sycamore Well #20 – replaced motor starter lugs	N – N55-P10 – installed new Worcester automatic valve operator assembly			N – N41-P1 unit #4 & moss screen – replaced control fuses
							N – S64-P1 moss screen – replaced control fuses

Well Facility Improvements (Repairs-R or New-N)							
Transformers (number)	**Thermal Overloads**	**Lightning Arrestor**	**Panel wiring / Circuit Breaker /Cont**	**Soft Start Equip-ment**	**Control Fuses**	**Relays / Switches**	**12KV Fuses**
			N – Sycamore Well #23 – replaced 600A circuit breaker				N – NCSB Well #11- replaced primary 25A fuses

Additional Activities

- Retrofitted and installed new exhaust fan assembly at Pumping Plants N1-P2, N55-P1, N55-P2 and N55-P3.
- Created and edited master SCADA remote monitoring.
- Oversaw the 12KV three (3) power poles replacement at North Canal Spreading Works Well #11 with contractor.
- Oversaw the 12KV four (4) power poles replacement at Sycamore Well #31 with contractor.
- Assisted contractor at Forrest Frick Pumping Plant for the fire suppressor installation.

FORREST FRICK PUMPING PLANT

- 11,242 AF of water was pumped during the month.

HOWARD FRICK PUMPING PLANT (AQUEDUCT INTERTIE)

- 0 AF was delivered to the District from the CA Aqueduct through the Howard Frick Pumping Plant/Pipeline and 0 AF was returned.

EXHIBIT "A-1"

ARVIN-EDISON WATER STORAGE DISTRICT

2026 WATER SUPPLY AND DEMAND

SUPPLY		***AF***	***%***
FRIANT-KERN (F-K)			
40,000 AF CLASS 1 (100%)		40,000	
URF TIER 1 BLOCK A (0.2% CLASS 2)		530	
URF TIER 1 BLOCK B (0.7% CLASS 2)		2,224	
URF TIER 2 BLOCK AA (3.66% CLASS 2)		11,409	
WATER QUALITY MITIGATION (NKWSD)		110	
CARRYOVER OF 2025 WATER		4,439	
	SUBTOTAL	58,712	
CHOWCHILLA WSD EXCHANGE (URF/CLASS 1)		728	
KERN TULARE EXCHANGE		-10,109	
CHOWCHILLA WSD EXCHANGE (SJRRP/CLASS 1/URF)		-5,549	
DELANO-EARLIMART IRRIGATION DISTRICT (HOMER RETURN)		-2,031	
KAWEAH DELTA WCD (HOMER RETURN)		-609	
FRESNO COUNTY		-550	
	SUBTOTAL	-18,120	
	TOTAL F-K	40,592	28.9%
CROSS VALLEY CANAL (CVC)			
SJRPP RECAPTURE RECIRCULATION		13,153	
ROSEDALE WSD		5,000	
KERN TULARE/ ID4 EXCHANGE		10,000	
METROPOLITAN WD (WQSA)		3,150	
FRESNO COUNTY (25% CVP)		750	
DEWATER CANAL		127	
DROUGHT POOL PROGRAM		-168	
SLR 1% EVAPORATION & LOSSES		-294	
	TOTAL CVC	31,718	22.6%
SJRPP (RECAPTURED WATER)			
CHOWCHILLA WATER DISTRICT		7,250	
MADERA IRRIGATION DISTRICT		4,689	
DEL PUERTO WATER STORAGE DISTRICT		-3,685	
		8,254	5.9%
STATE WATER PROJECT (AQUEDUCT)			
KT EXCHANGE		0	
	TOTAL AQUEDUCT	0	0.0%
INTERTIE PIPELINE (IPL)			
METROPOLITAN WD (WQSA)		1,092	
	TOTAL IPL	1,092	0.8%
KERN RIVER			
CITY OF BAKERSFIELD		4,995	
	TOTAL KERN RIVER	4,995	3.6%
TOTAL IMPORT		**86,651**	**61.7%**
GROUNDWATER PUMPING			
IRRIGATION DEMAND		53,822	
	TOTAL PUMPING	53,822	38.3%
TOTAL WATER SUPPLY		**140,473**	**100.0%**

DEMAND		
IRRIGATION DEMAND (MARCH -JUNE '26)	60,240	42.9%
IRRIGATION DEMAND (JULY- FEBRUARY '27)	67,800	48.3%
SPREADING (MARCH - JUNE '26)	2,883	2.1%
SPREADING (JULY-FEBRUARY '27)	0	0.0%
USBR CARRYOVER TO 2027	4,000	2.8%
LOSSES/METERING INACCURACIES	5,550	4.0%
TOTAL DEMAND	**140,473**	**100.0%**

Exhibit "A-2"

ARVIN-EDISON WATER STORAGE DISTRICT

2026 WATER MANAGEMENT

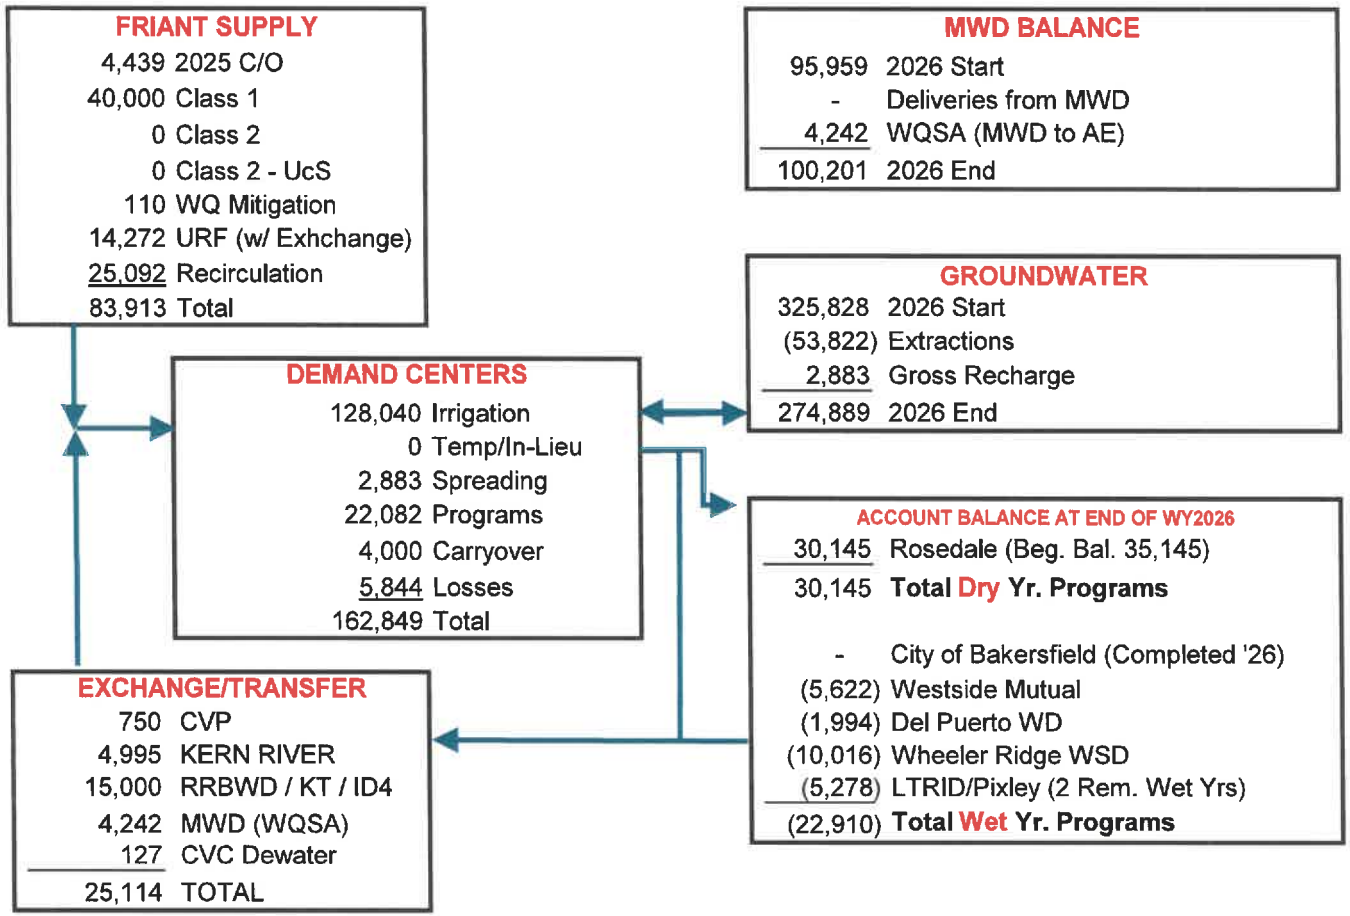

Surface Water	74,218	58%
Groundwater (33% of Max)	53,822	42%

EXHIBIT B-1
ARVIN-EDISON WATER STORAGE DISTRICT
2026 WATER YEAR DELIVERIES BY UNIT

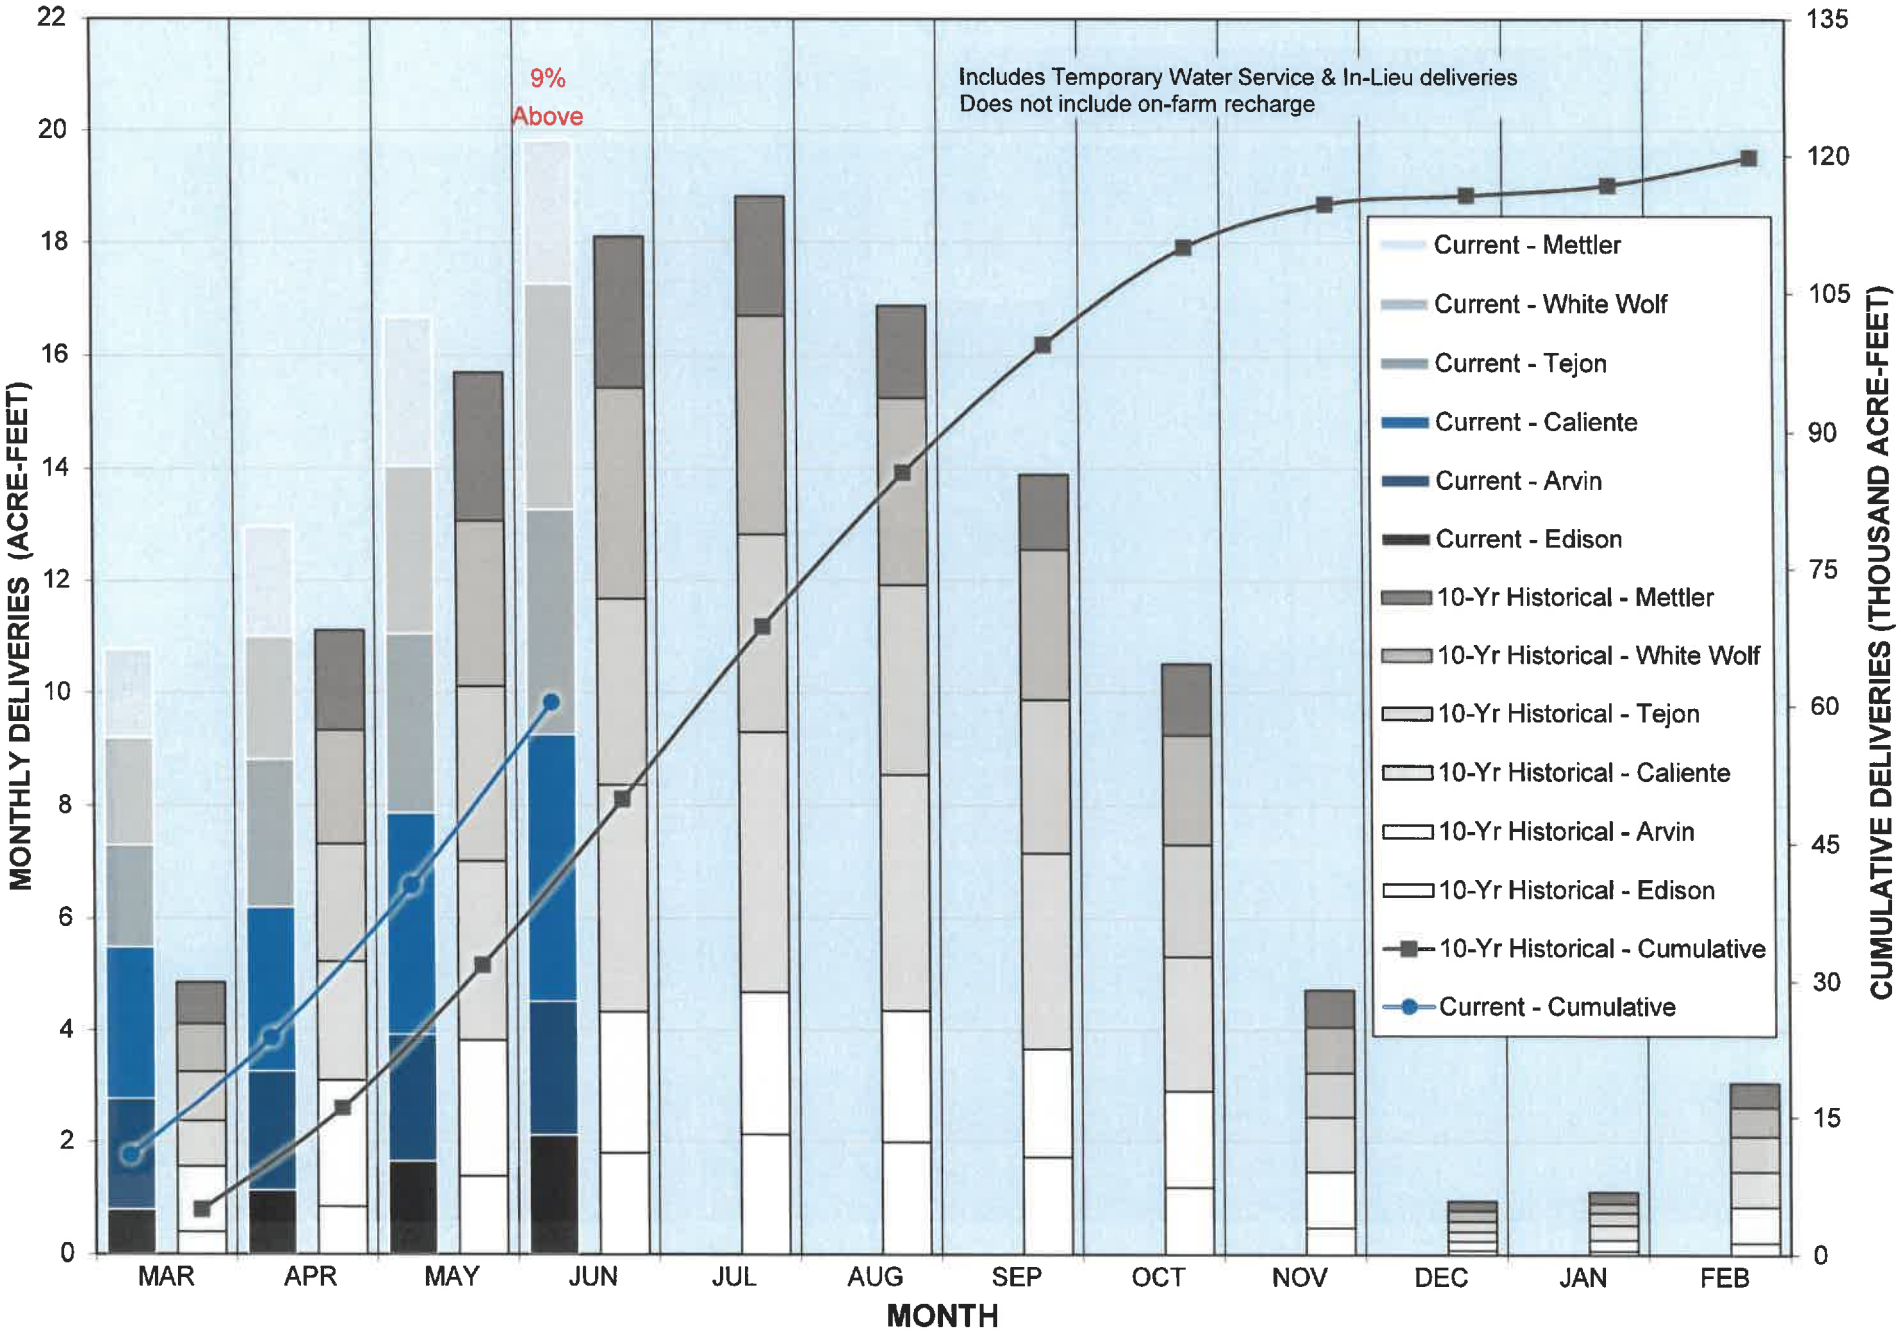

EXHIBIT B-2

ARVIN-EDISON WATER STORAGE DISTRICT

HISTORIC JUNE DELIVERIES BY YEAR

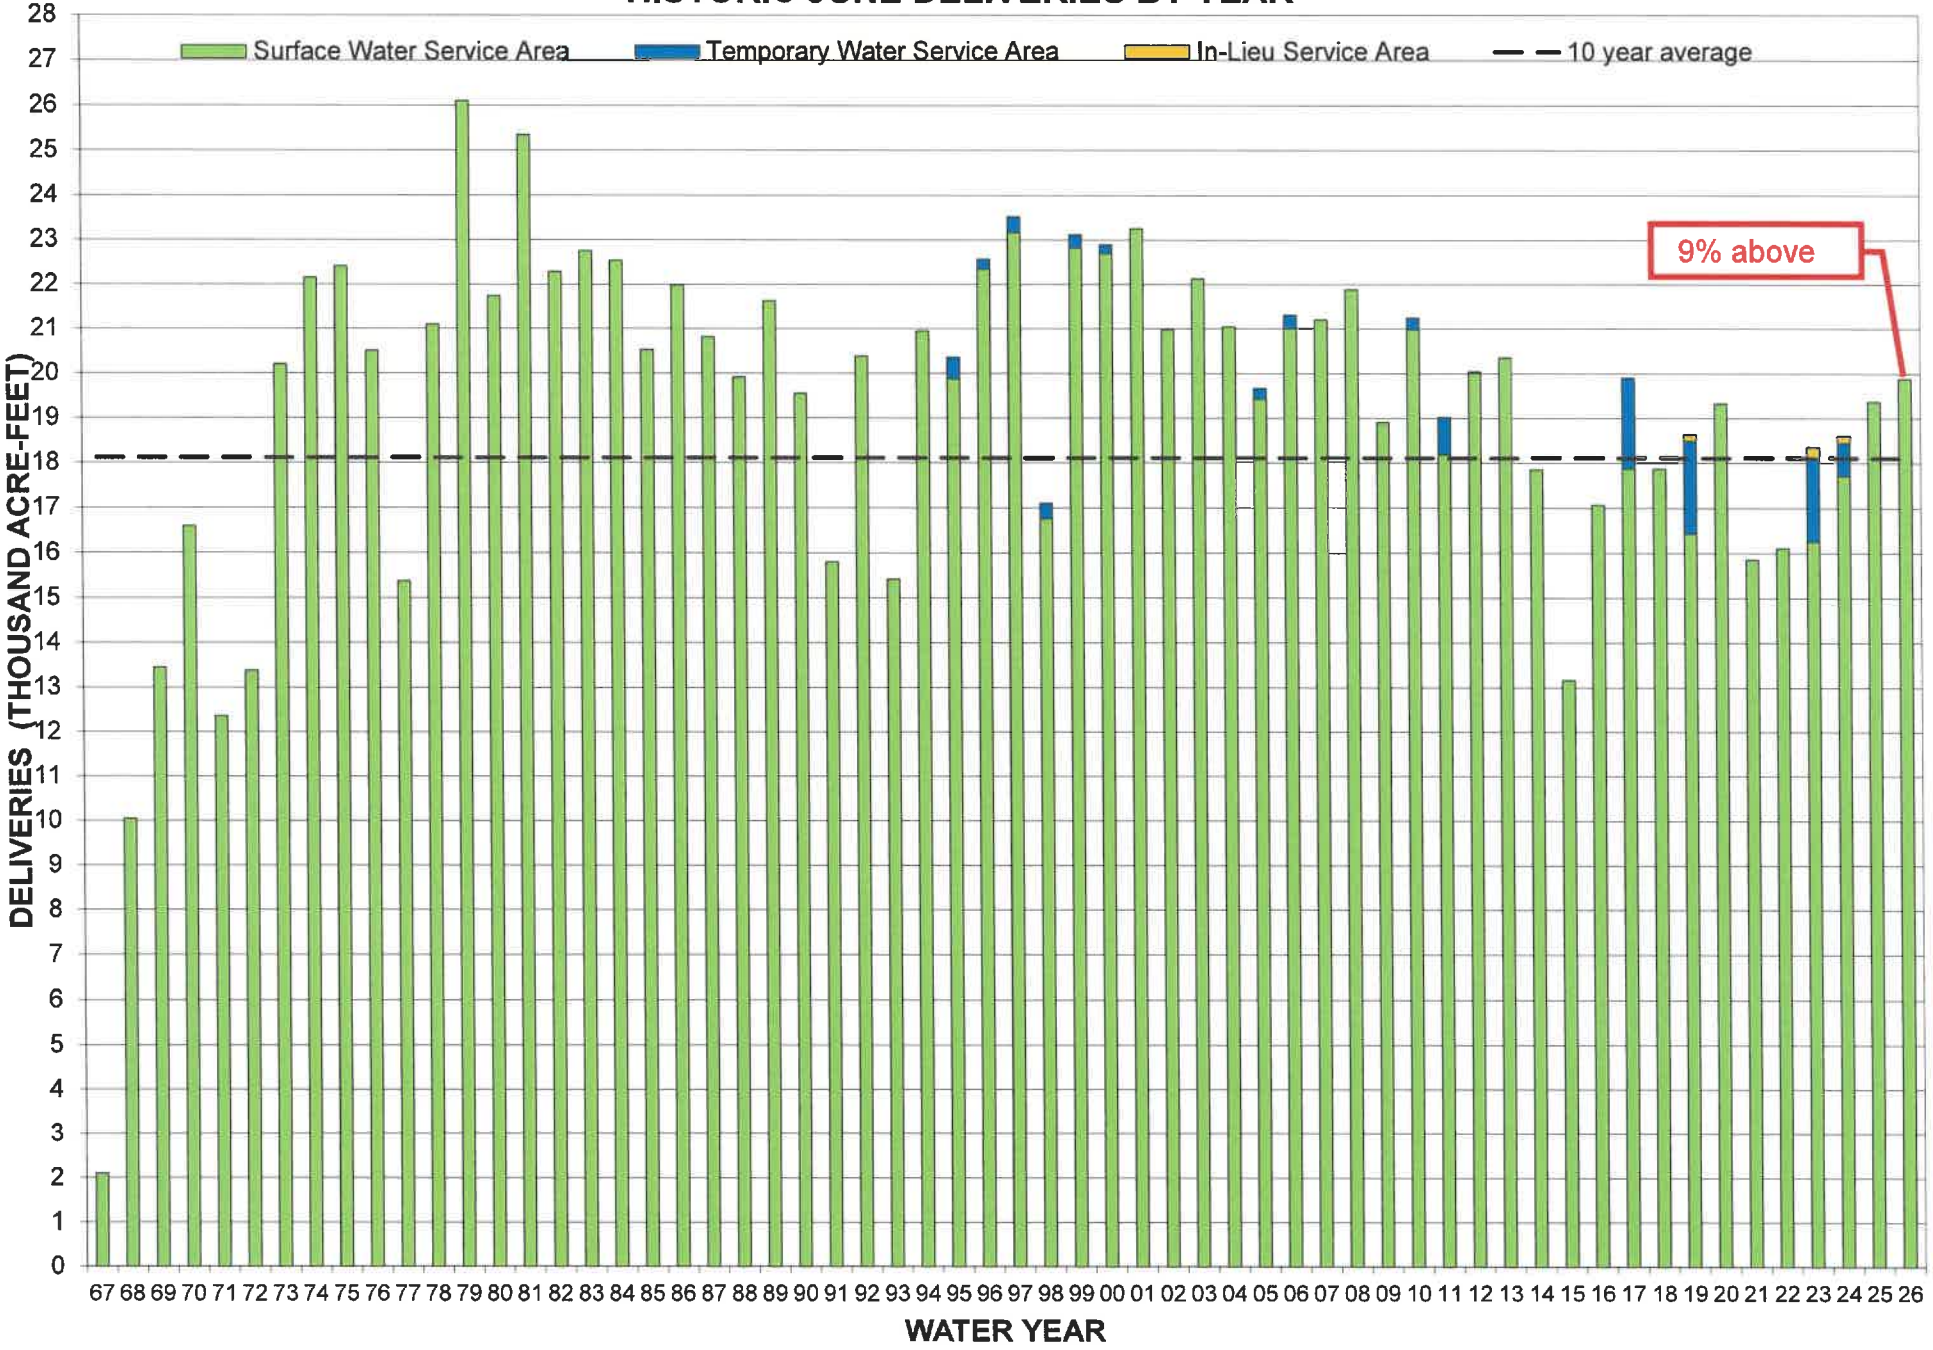

EXHIBIT B-3

ARVIN-EDISON WATER STORAGE DISTRICT

HISTORIC JUNE DELIVERIES BY MAGNITUDE

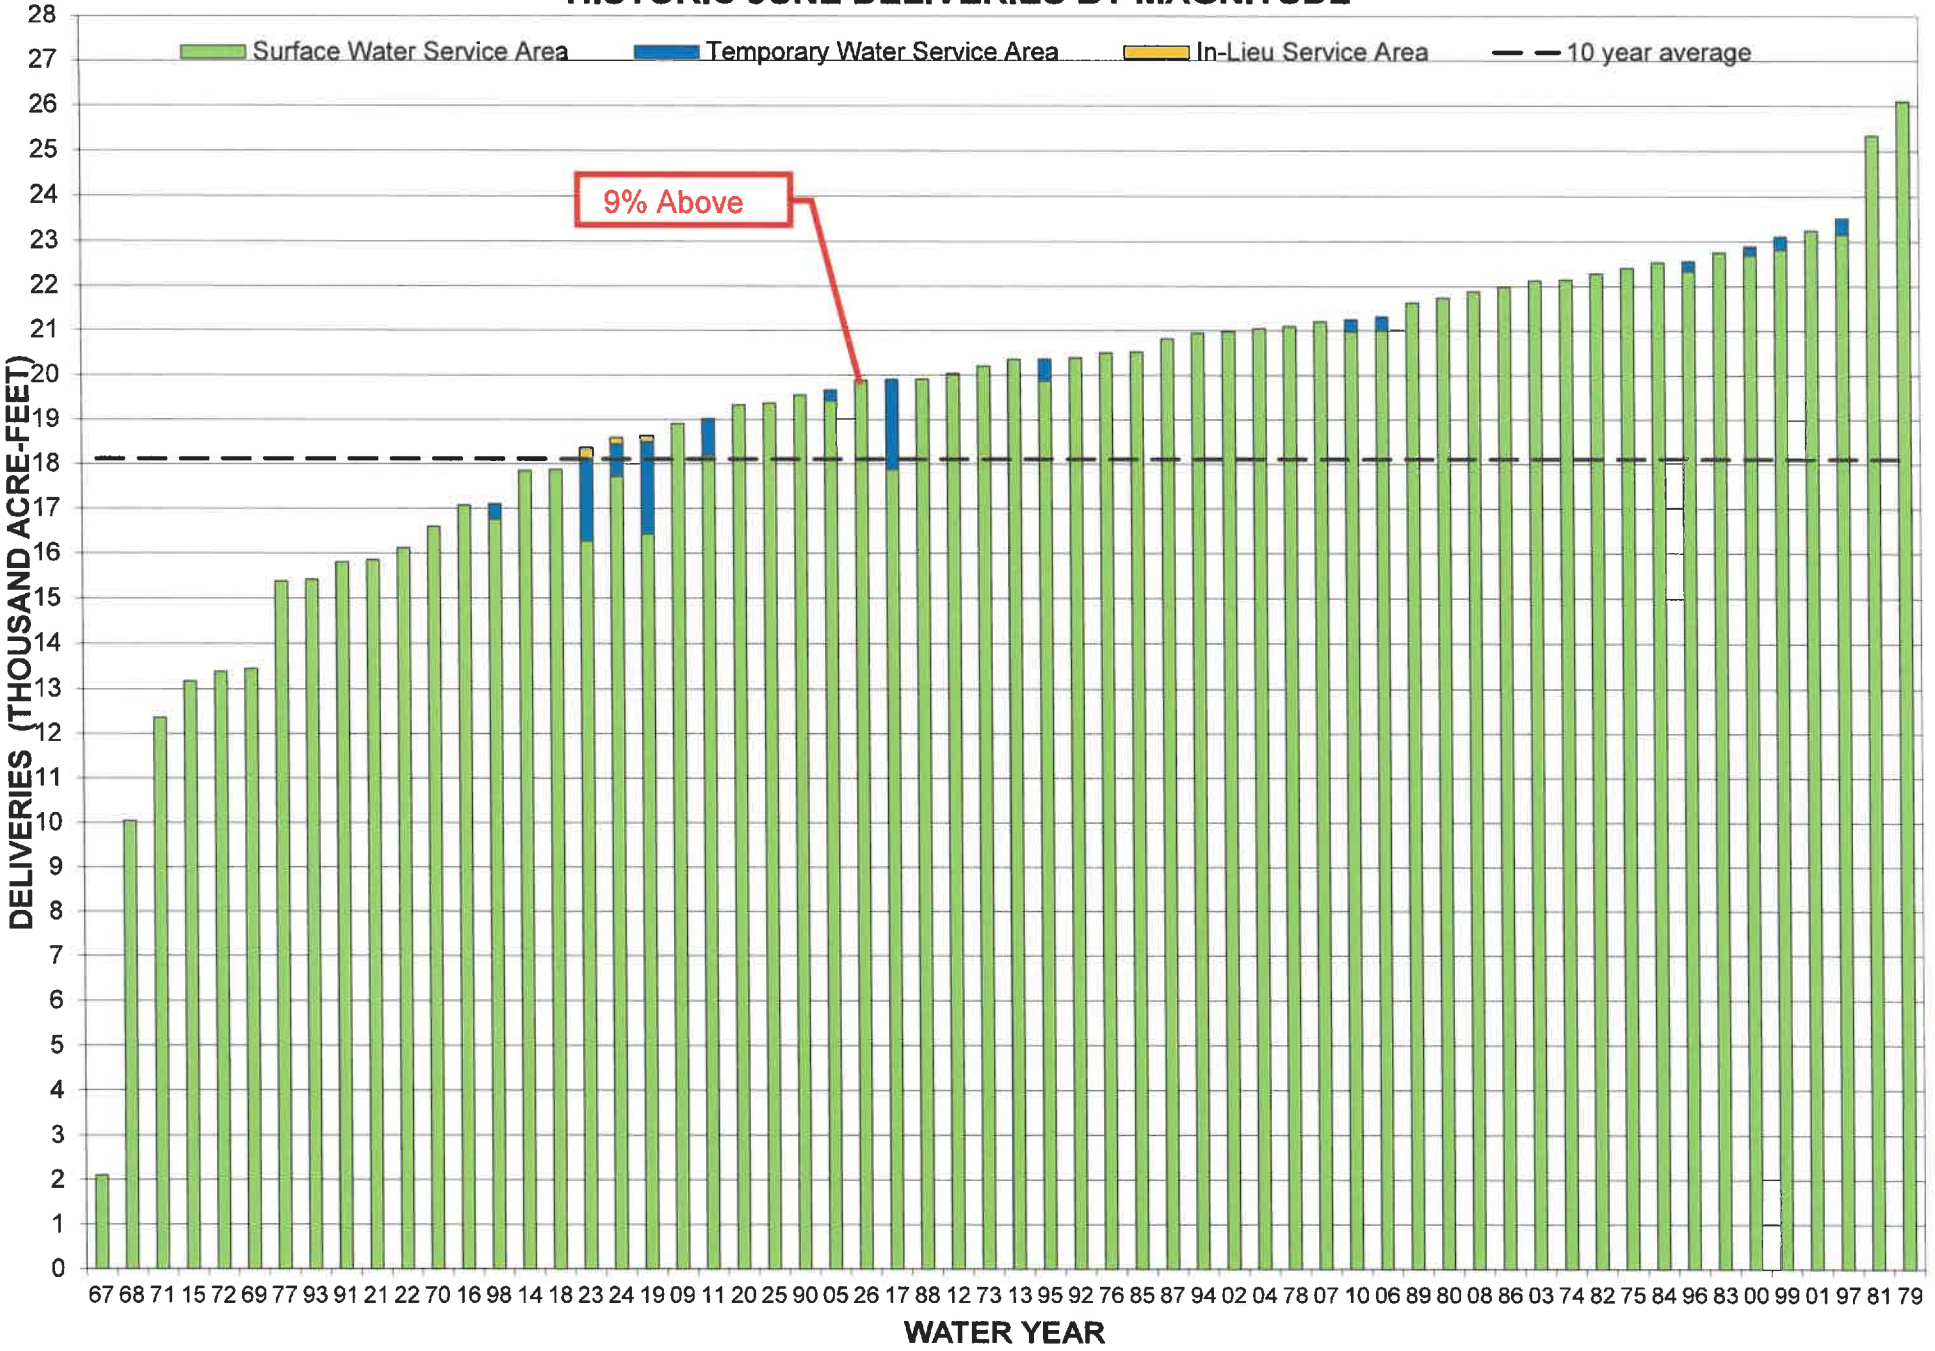

EXHIBIT "C-2"

ARVIN-EDISON WATER STORAGE DISTRICT

2026 AQUATIC PEST CONTROL TREATMENTS TO CANALS & SPREADING BASINS

Treatment Weeks (Monday)		Temps
JAN	01/05/26	40-60
	01/12/26	
	01/19/26	
	01/26/26	
FEB	02/02/26	44-67
	02/09/26	
	02/16/26	
	02/23/26	
MAR	03/02/26	51-84
	03/09/26	
	03/16/26	
	03/23/26	
	03/30/26	
APR	04/06/26	46-72
	04/13/26	
	04/20/26	
	04/27/26	
MAY	05/04/26	64-94
	05/11/26	
	05/18/26	
	05/25/26	
JUN	06/01/26	62-96
	06/08/26	
	06/15/26	
	06/22/26	
	06/29/26	
JUL	07/06/26	
	07/13/26	
	07/20/26	
	07/27/26	
AUG	08/03/26	
	08/10/26	
	08/17/26	
	08/24/26	
	08/31/26	
SEPT	09/07/26	
	09/14/26	
	09/21/26	
	09/28/26	
OCT	10/05/26	
	10/12/26	
	10/19/26	
	10/26/26	
NOV	11/02/26	
	11/09/26	
	11/16/26	
	11/23/26	
	11/30/26	
DEC	12/07/26	
	12/14/26	
	12/21/26	
	12/28/26	

Intake	North						South													
Stine Siphon	Bal. Res.	PP 24P1	NCSW	PP 41P1	PP 55P1	Syc. Ponds	Syc. Check	PP 32P1	PP 38P1	Tej. Ponds	Tej. Check	615 Check	729 Check	883 Check	Spill Way	Intertie Forbay
353+87	145+00	237+00	326+50	413+10	546+00	576+50	664+30	291+50	386+30		458+40	615+00	729+10	883+00	885+45	900+27
							102									
					10		56	56								
						45			38			26				
									34			35				

2026 Cost To Date	Treatment	Material	Labor	Total
	Captain/Nautique	$0	$0	$0
	Phycomycin	$0	$0	$0
	Cascade	$0	$0	$0
	Teton/Hydrothol	$51,563	$4,588	$56,151
	Spreading Basins	$0	$0	$0
	Total	$51,563	$4,588	$56,151

Shaded weeks are actual
Copper treatment (gal/lbs) for algae and pondweed (injected/broadcast)
Phycomycin (hydrogen peroxide) treatment (lbs) for algae (broadcast)
Endothall treatment (gal) for milfoil/basins (injected)
Endothall treatment (gal) for algae (injected)
Sonar/Clearcast/RoundUp Custom/MSO (gal)
Winter Maintenance

Year	2026	2025	2024	2023	2022	2021	2020	2019	2018	2017	2016	2015	2014	2013	2012	2011	2010	2009	2008	2007	2006
Year Type	Normal-Dry	Dry	Normal-Wet	Wet	Normal-Dry	Critical-High	Dry	Wet	Normal-Dry	Wet	Normal-Dry	Critical-Low	Critical-High	Dry	Dry	Wet	Normal-Wet	Normal-Wet	Normal-Dry	Dry	Wet
Amount	$56,151	$170,102	$88,978	$253,046	$461,593	$420,296	$399,808	$105,928	$235,599	$222,685	$186,034	$262,734	$367,563	$528,770	$504,159	$233,449	$24,969	$226,466	$341,506	$464,165	$341,920

Average by WY Type	Critical-High	Critical-Low	Dry	Normal-Dry	Normal-Wet	Wet
	$393,929	$262,734	$474,226	$232,694	$113,471	$192,838

EXHIBIT "D"

ARVIN-EDISON WATER STORAGE DISTRICT

SUMMARY OF CLIMATOLOGICAL OBSERVATIONS

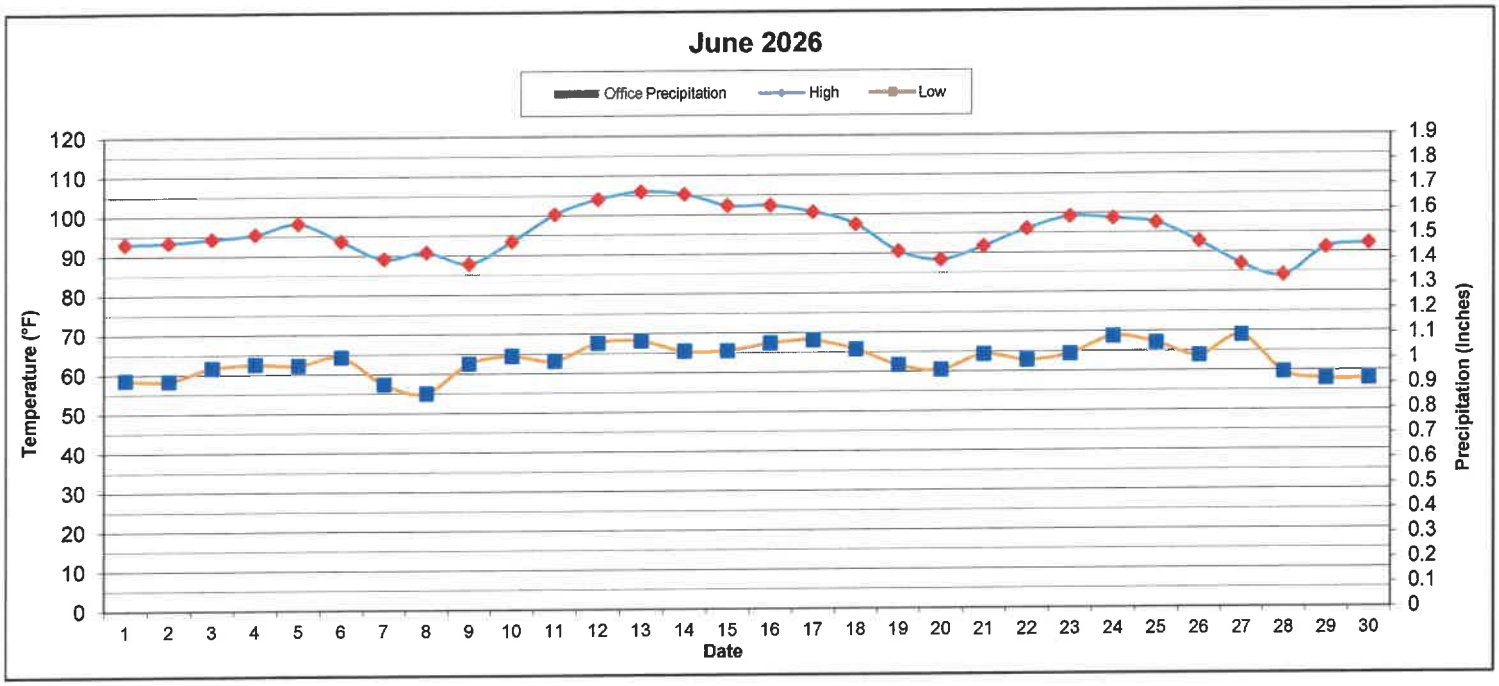

PRECIPITATION	BAL RES (1)		OFFICE (2)		SYCAMORE (3)		TEJON (4)		INTERTIE (5)	
	INCHES	% AVG.	INCHES	% AVG.	INCHES	% AVG.	INCHES	% AVG.	INCHES	% AVG.
AVG. MONTHLY	0.07		0.09		0.07		0.08		0.06	
AVG. YEAR TO DATE	7.59		8.60		8.25		7.28		7.99	
CURRENT MONTH	0.00	0%	0.00	0%	0.00	0%	0.00	0%	0.08	133%
CUMULATIVE (07/01/25 - 06/30/26)	8.82	116%	10.03	117%	9.09	110%	8.19	113%	7.97	100%

TEMPERATURE (6)	(°F)	DATE	TIME
MAXIMUM TEMPERATURE	106	6/13/2026	4:00 PM
AVERAGE MAXIMUM TEMPERATURE	95		
# DAYS THIS MONTH ABOVE 100 °F	7		
MINIMUM TEMPERATURE	55	6/8/2026	4:00 AM
AVERAGE MINIMUM TEMPERATURE	63		
# DAYS THIS MONTH BELOW 32 °F	0		

WIND (6)	M.P.H.	DATE	TIME	DRCTN
MAXIMUM WIND SPEED	5.3	6/27/2026	6:30 PM	NE
AVERAGE WIND SPEED	4.4			
AVERAGE WIND SPEED @ 8:00 AM	4.3			

BAROMETRIC PRESSURE (7)	IN. HG	DATE	TIME
AVERAGE PRESSURE @ 8:00 AM	29.38		
MAXIMUM PRESSURE	29.50	6/3/2026	9:00 AM
MINIMUM PRESSURE	29.20	6/5/2026	8:00 PM

NOTES

(1) October 2018 to Present data gathered from District rain gauges
(2) 1975 to Present data gathered from District rain gauges
(3) 1968 to Present data gathered from District rain gauges
(4) 1967 to Present data gathered from District rain gauges
(5) October 2018 to Present data gathered from District rain gauges
(6) Data retrieved from CIMIS (http://www.cimis.water.ca.gov/WSNReportCriteria.aspx) (125 Arvin-Edison)
(7) Data retrieved from Weather Underground (https://www.wunderground.com/us/ca/arvin/zmw:93203.1.99999)
Precipitation Day is 8:00 AM to 8:00 AM

EXHIBIT "E"

ARVIN-EDISON WATER STORAGE DISTRICT

WY2026 ENERGY CONSUMPTION AND POWER DEMAND

	ENERGY CONSUMED - KWH						TOTAL DEMAND - KW						
Month	Forrest Frick PP	Distrib. System	Spreading	Wells	Intertie PP	Total	Forrest Frick PP	Distrib. System	Spreading	Wells	Intertie PP	Total	Load Factor
MAR 26	1,886,197	3,726,551	140,493	2,874,159	4,164	8,631,563	4,609	15,575	1,174	6,934	7	28,299	41%
APR	1,102,059	4,048,867	17,003	6,466,280	3,981	11,638,191	4,021	15,357	355	10,188	8	29,929	54%
MAY	2,180,090	5,315,235	22,390	5,858,928	4,371	13,381,014	5,468	15,110	352	8,503	9	29,441	61%
JUN	2,456,371	5,747,624	18,175	5,745,536	4,267	13,971,972	5,309	14,778	353	9,070	8	29,519	66%
JUL													
AUG													
SEP													
OCT													
NOV													
DEC													
JAN 27													
FEB													
TOTAL	7,624,716	18,838,277	198,061	20,944,902	16,783	47,622,739							

Notes: - Since 2005 KW records reflect non-simultaneous demands. 7/6/2026

- Energy use for lighting accounts for approximately 90,000 kWh/month at District wellfields and 4,000 kWh/month at the Intertie Pumping Plant

EXHIBIT "F"

ARVIN-EDISON WATER STORAGE DISTRICT

2026 WATER YEAR WELLFIELD PRODUCTION - AF

Month	Bal Res		North Canal 6		Wellfield						Total		
					North		Sycamore		Tejon				
	AF	% of Historical Max	AF	% of Historical Max	AF	% of Historical Max	AF	% of Historical Max	AF	% of Historical Max	AF	AF / Day	% of Historical Max
MAR - 26	0	0%	485	40%	1,601	62%	1,467	22%	345	6%	3,898	126	25%
APR	0	0%	1,082	90%	2,731	90%	3,335	48%	984	20%	8,132	271	55%
MAY	0	0%	978	79%	2,722	74%	3,245	45%	601	11%	7,545	243	50%
JUN	0	0%	953	47%	2,611	71%	3,011	150%	572	29%	7,147	231	47%
JUL	0	0%	0	0%	0	0%	0	0%	0	0%	0	0	0%
AUG	0	0%	0	0%	0	0%	0	0%	0	0%	0	0	0%
SEP	0	0%	0	0%	0	0%	0	0%	0	0%	0	0	0%
OCT	0	0%	0	0%	0	0%	0	0%	0	0%	0	0	0%
NOV	0	0%	0	0%	0	0%	0	0%	0	0%	0	0	0%
DEC	0	0%	0	0%	0	0%	0	0%	0	0%	0	0	0%
JAN - 27	0	0%	0	0%	0	0%	0	0%	0	0%	0	0	0%
FEB	0	0%	0	0%	0	0%	0	0%	0	0%	0	0	0%
Total	0		3,498		9,665		11,058		2,502		26,723	73	15%
Ratio	0%		13%		36%		41%		9%		100%	Average	
Wells	4		6		15		34		29		88		
AF/Well	0		583		644		325		86		304		

EXHIBIT "G-1"

ARVIN-EDISON WATER STORAGE DISTRICT

2026 WATER YEAR GROSS SPREADING - AF

Month	Eastside Canal Sunset	Bal Res	North Gravity	North Pressure	Sycamore	Tejon Gravity	Tejon Pressure	District Land Caliente	Landowner Recharge [1]	Subtotal	In-Lieu	Temporary Water	Total
MAR-26	0	67	794	260	153	920	251	0	0	2,445	0	0	2,445
APR	0	120	0	0	0	0	0	0	0	120	0	0	120
MAY	0	232	0	0	0	0	3	0	0	235	0	0	235
JUN	0	80	0	0	0	0	3	0	0	83	0	0	83
JUL	0	0	0	0	0	0	0	0	0	0	0	0	0
AUG	0	0	0	0	0	0	0	0	0	0	0	0	0
SEP	0	0	0	0	0	0	0	0	0	0	0	0	0
OCT	0	0	0	0	0	0	0	0	0	0	0	0	0
NOV	0	0	0	0	0	0	0	0	0	0	0	0	0
DEC	0	0	0	0	0	0	0	0	0	0	0	0	0
JAN-27	0	0	0	0	0	0	0	0	0	0	0	0	0
FEB	0	0	0	0	0	0	0	0	0	0	0	0	0
Total	0	499	794	260	153	920	257	0	0	2,883	0	0	2,883
Ratio													
Ratio													

Total Pressure		499		260			257			1,016			1,016

EXHIBIT "H-1"

ARVIN-EDISON WATER STORAGE DISTRICT

STATIC VS PUMPING WATER LEVELS IN DISTRICT WELLS - JUN 2026

ALL VALUES IN FEET

	WELL #	STATIC LEVEL	PUMPING LEVEL	BOWL [1] DEPTH	TOTAL DEPTH	DRAW [2,3] DOWN	BOWL [4] COVERAGE
NORTH CANAL (26)	N1	474	581	610	840	107	29
	N2	448	578	700	840	129	122
	N3	391	416	610	840	25	194
	N4	441	467	550	864	25	83
	N5	356	368	550	864	12	182
	N6	460	503	640	900	43	137
	N7	468	496	600	990	28	104
	N8	412	458	560	950	46	102
	N9	448	557	700	970	109	143
	N10	433	503	560	1020	70	57
	N11	416	472	562	1000	55	90
	N12	468	496	600	1010	28	104
	N13	408	438	540	980	30	102
	N14	443	466	540	928	23	74
	N15	386	531	700	1190	146	169
	N16	404	518	610	1198	114	92
	N17	N/A	N/A	610	1190	N/A	N/A
	N18	352	412	610	1180	60	198
	N19	469	515	760	1360	46	245
	N20	483	543	820	1020	60	277
	N21	446	536	660	950	90	124
	N22	449	474	680	1000	25	206
	N23	439	460	720	1030	21	260
	N24	449	472	710	1000	23	238
	N26	460	487	760	1290	28	273
	Avg	434	489				

	WELL #	STATIC LEVEL	PUMPING LEVEL	BOWL [1] DEPTH	TOTAL DEPTH	DRAW [2,3] DOWN	BOWL [4] COVERAGE
TEJON (29)	71	495	527	800	1068	32	273
	72	481	497	800	1087	16	303
	73	484	520	800	1068	37	280
	74	481	527	800	1068	46	273
	75	484	504	800	1068	21	296
	76	471	520	700	1032	49	180
	77	467	537	800	1056	69	263
	78	465	518	800	1044	53	282
	79	564	666	800	1032	102	134
	80	467	560	800	996	92	240
	81	358	402	700	996	44	298
	82	367	416	700	996	49	284
	83	438	N/A	N/A	N/A	N/A	N/A
	84	360	388	700	996	28	312
	86	504	537	800	996	32	263
	87	500	527	800	984	28	273
	88	500	532	800	948	32	268
	89	484	518	800	996	35	282
	90	557	596	700	996	39	104
	92	514	567	800	980	53	233
	93	514	532	800	1050	18	268
	94	574	675	860	1050	102	185
	95	458	N/A	N/A	N/A	N/A	N/A
	96	490	648	800	1100	157	152
	98	515	566	760	1340	51	194
	99	479	517	760	1340	38	243
	100	474	516	800	1340	42	284
	101	454	523	740	1310	69	217
	102				1310		
	Avg	481	532				

	WELL #	STATIC LEVEL	PUMPING LEVEL	BOWL [1] DEPTH	TOTAL DEPTH	DRAW [2,3] DOWN	BOWL [4] COVERAGE
SYCAMORE (35)	1	384	421	645	800	37	224
	2	224	364	570	879	141	206
	4	462	499	700	876	37	201
	5	447	482	690	840	35	208
	6	410	480	690	886	69	210
	7	451	511	700	850	60	189
	8	450	N/A	N/A	N/A	N/A	N/A
	9	462	511	700	500	49	189
	10	445	482	690	886	37	208
	11	444	487	700	910	44	213
	12	462	501	700	898	39	199
	13	N/A	N/A	690	850	N/A	N/A
	14	403	447	680	850	44	233
	15	454	583	710	850	129	127
	16	451	566	700	898	116	134
	17	403	606	650	850	203	44
	18	507	548	650	850	42	102
	20	441	477	690	804	37	213
	21	427	503	690	910	76	187
	22	421	453	610	792	32	157
	23	418	450	600	792	32	150
	24	418	448	570	792	30	122
	25	430	458	610	792	28	152
	26	415	487	690	816	72	203
	28	324	389	590	792	65	201
	29	431	475	690	792	44	215
	31	434	496	660	744	62	164
	32	N/A	N/A	660	744	N/A	N/A
	33	464	566	700	793	102	134
	34	437	N/A	N/A	N/A	N/A	N/A
	35	460	538	700	800	79	162
	36	435	472	600	730	37	128
	37	427	459	540	820	32	81
	38	438	494	880	1270	56	383
	39				1190		
	Avg	426	488				

MONTHLY SUMMARY - AVERAGE WATER LEVELS						
READINGS	STATIC LEVELS			PUMPING LEVELS		
END OF	N. CANAL	SYCAMORE	TEJON	N. CANAL	SYCAMORE	TEJON
JUN-25	436	423	489	495	480	545
JUL	435	420	489	495	476	544
AUG	436	423	487	496	478	541
SEP	436	421	483	494	477	537
OCT	429	413	469	487	468	524
NOV	423	403	458	481	458	512
DEC	421	399	449	479	454	504
JAN	419	397	443	478	452	498
FEB	418	395	440	476	450	494
MAR	425	416	460	481	472	513
APR	431	422	467	487	480	518
MAY	432	427	475	488	488	526
JUN-26	434	426	481	489	488	532
12 MONTH CHANGE	+02	-03	+08	+06	-08	+13

OUT OF SERVICE (2)
AIRLINE FAILURE, ACCOUSTIC SOUNDER USED (15)
MONITORING WELLS (4)
UNSTABLE DATA (1)
NEW WELLS PENDING (2)

[1] Bowl depth is measured from the bottom of the bowls to top of the pump.
[2] When pumps aren't running,pumping levels are estimated based on previous draw down records. (6 month avg.)
[3] Red numbers indicate drawdowns that are above 100.
[4] Red numbers indicate bowl coverage that is below 50.

EXHIBIT "H-2"

ARVIN-EDISON WATER STORAGE DISTRICT

WELLFIELD PUMPING WATER LEVELS - 2007, 2015, 2020, 2022-26

NORTH CANAL

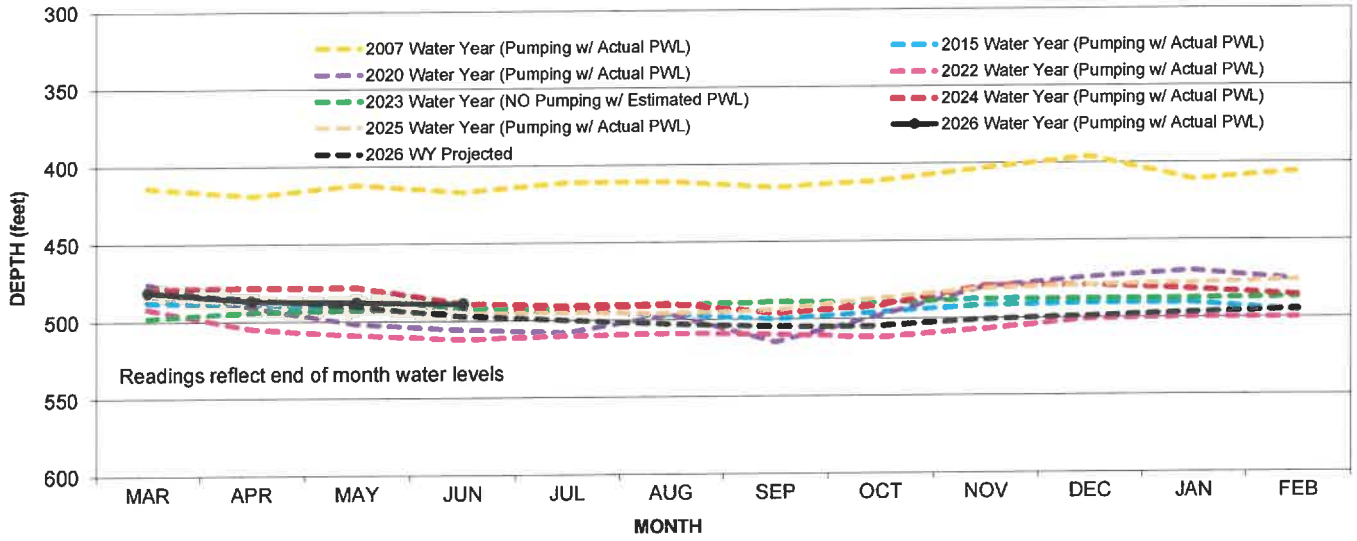

SYCAMORE WELLFIELD

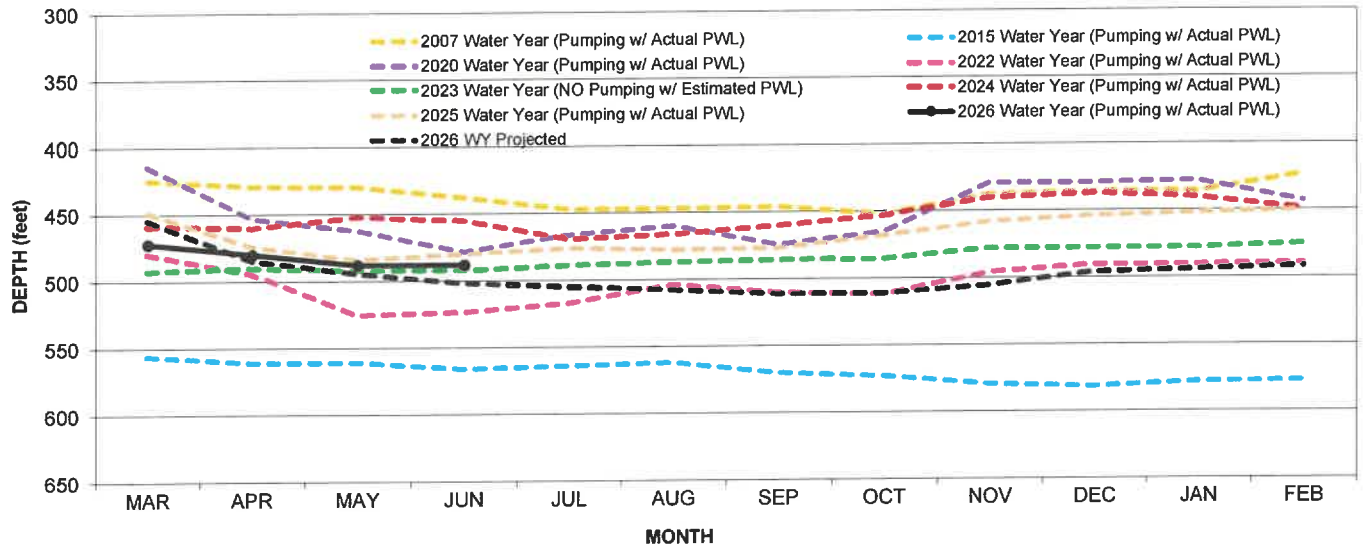
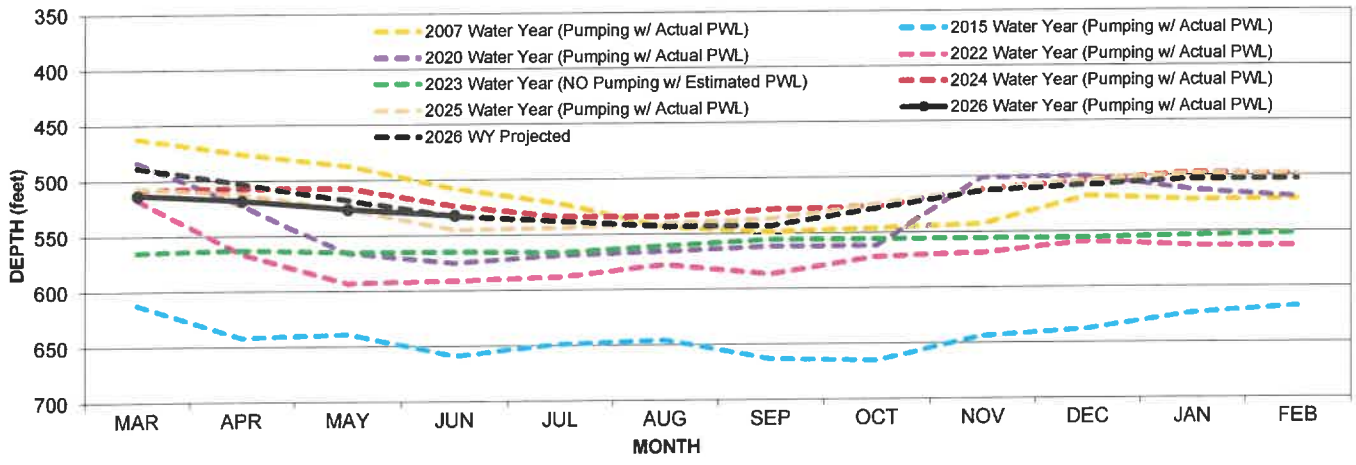
TEJON WELLFIELD
